Saugerties Central School District Saugerties, New York

# Capital Projects Update Board of Education



TELCOMES YOL









### Agenda

- 1. Capital Improvement Project
- 2. Energy Performance Contract Project
- 3. '21-'22 Capital Outlay Project
- 4. Questions?












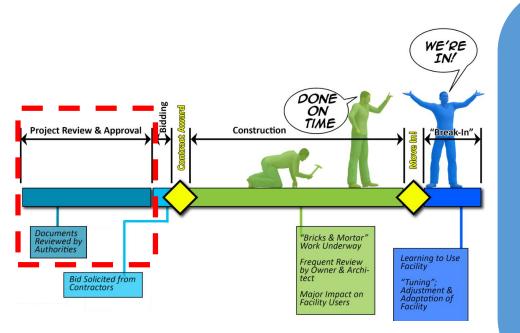

#### **Ongoing Pre-Bid Phase Tasks**

#### Front Ends:

- Establish Prime Contracts (GC, PC, HC, EC, etc.)
- Assignment of Work
- Project Milestone Schedule
- Temporary Phasing / Conditions
- Coordination of Consultant Data
- SHPO No Exceptions to Cahill Work!!
- Code Variance Ongoing Conversations with SED to Determine Requirements
- ✤ QA/QC Review of Documents.

#### Ongoing Tasks:

Submission Logged in to Office of Facilities Planning (SED) on 11/2/2021.

Arch & Engineering reviews are currently noted on website as approx. 6-8 weeks, but Approval timeframe will vary based on their workload.

Review Meeting with Owner, Tetra Tech & BBL on 12/15/2021.










#### Capital Project Overall Timeline

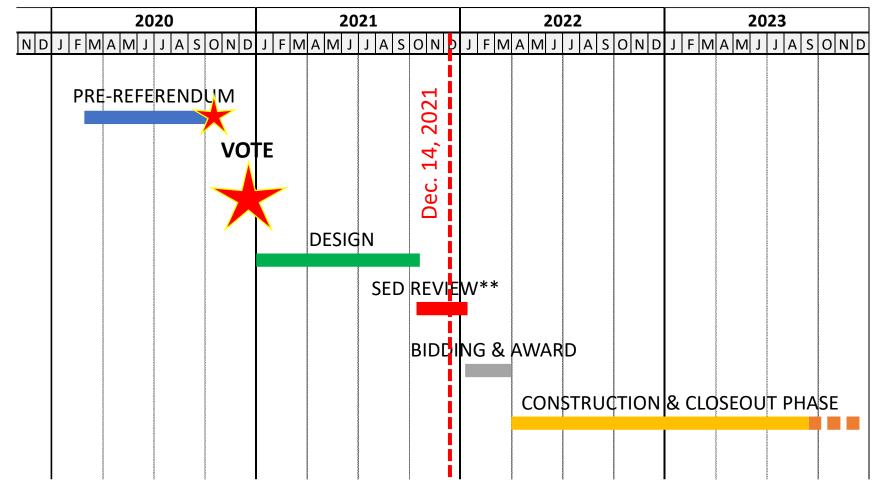

\*\* SED Review times vary.










#### Energy Performance Contract (EPC) Project

- SED Engineering Technical Review Completed 10-18-2021. Awaiting SED PM Review to Obtain Full Project Approval.
- Next Steps: District RFPs for Financing. ESCO Finalization of Scope Dependent Upon SED Approval. Schedule to be Updated & Coordinated with Capital Project.

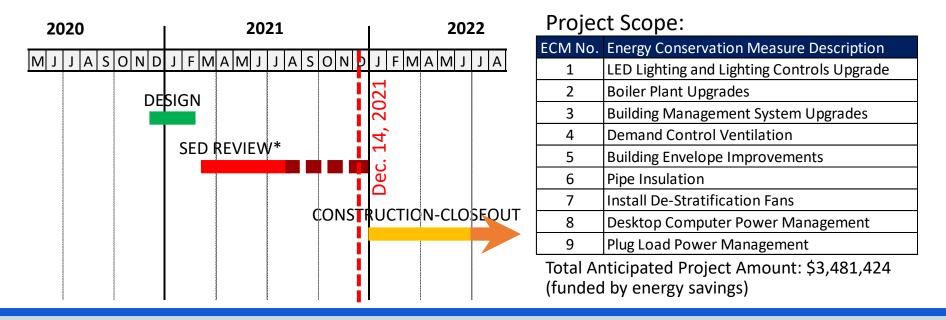

Sauger

CENTRAL SCHOOL DISTRICT






# Capital Outlay Project Update

## '21-'22 Project at Riccardi Elem. School - Flooring

- Flooring Replacement in Select Classrooms and Corridors
- Will Involve Abatement Design by Quest.
- Project in Early Design Phase



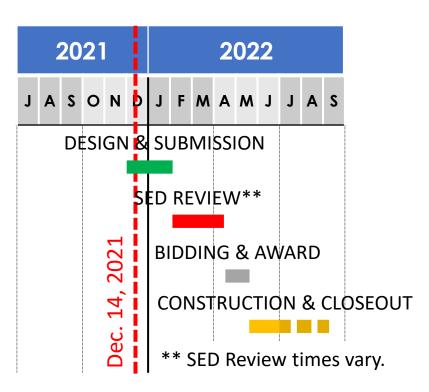









"Children are the World's most valuable resource and its best hope for the future." ~John F. Kennedy

#### **Ongoing Community Updates:**

- Visitation-Facilities Committee, Board of Education
- District's website:
  - https://www.saugerties.k12.ny.us/Domain/930



Saugerties CENTRAL SCHOOL DISTRICT

